ID	Task Name	Duration	Start	Finish	Resource Names
0	**104 Cameron Road**	**205 days**	**Mon 4/08/25**	**Thu 21/05/26**	
1	**1 Site Establishment**	**2 days**	**Mon 4/08/25**	**Tue 5/08/25**	
2	1.1 Set up site fencing, signage and hazard boards	1 day	Mon 4/08/25	Mon 4/08/25	BUCO
3	1.2 Disconnect and make safe all required electrical items	1 day	Tue 5/08/25	Tue 5/08/25	EMAC
4	1.3 Disconnect and isolate all required plumbing items	1 day	Tue 5/08/25	Tue 5/08/25	PLUMBING WORKS
5	1.4 Establish existing car parks to remain for other leases and make accessible for duration	1 day	Tue 5/08/25	Tue 5/08/25	BUCO
6	**2 Pre BC Works**	**59 days**	**Tue 5/08/25**	**Fri 24/10/25**	
7	2.1 Remove outdated or redundant HVAC, plumbing and electrical systems	2 days	Wed 6/08/25	Thu 7/08/25	HIKO
8	2.2 Remove all walls, floor coverings and ceilings throughout	10 days	Wed 6/08/25	Tue 19/08/25	BUCO
9	2.3 Cut out and remove concrete floor and wall between grid lines A+B	5 days	Tue 5/08/25	Mon 11/08/25	COMPLETE CONCRETE CUTTING
10	2.4 Demolish raised concrete area to suit fitout and maintain level entry	5 days	Wed 20/08/25	Tue 26/08/25	DETAILED EXCAVATION,DETAILED EXCAVATION/BUCO
11	2.5 Demolish concrete ramp leading to the car park	5 days	Wed 27/08/25	Tue 2/09/25	DETAILED EXCAVATION,DETAILED EXCAVATION/BUCO
12	2.6 Set up Traffic management	1 day	Wed 20/08/25	Wed 20/08/25	COMPLETE TRAFFIC
13	2.7 Asbestos removal to soffit canopy and old soffit left inside the building	1 day	Thu 21/08/25	Thu 21/08/25	AR PLUS
14	2.8 Demolish existing canopy	10 days	Fri 22/08/25	Thu 4/09/25	BUCO
15	2.9 Remove traffic management	1 day	Fri 5/09/25	Fri 5/09/25	COMPLETE TRAFFIC
16	2.10 Trade precurement	5 days	Mon 20/10/25	Fri 24/10/25	BUCO
17	**3 Seismic Strengthening**	**65 days**	**Fri 24/10/25**	**Mon 26/01/26**	
18	3.1 Site measure and confirm falls for new pc aluminium gutter insert	0 days	Fri 24/10/25	Fri 24/10/25	ADCO
19	3.2 Structural steel site measure	0 days	Fri 24/10/25	Fri 24/10/25	ASSET ENGINEERING
20	3.3 SI confirming minor VO for steel collumn bases	0 days	Tue 28/10/25	Tue 28/10/25	SED
21	3.4 mark out concrete floor for service chases	1 day	Tue 28/10/25	Tue 28/10/25	PLUMBING WORKS/BUCO
22	3.5 Cut concrete floor and remove all required concrete	1 day	Wed 29/10/25	Wed 29/10/25	COMPLETE CONCRETE CUTTING/BUCO
23	3.6 Remove soil layer between concrete floor and foundation as per SI from SED	1 day	Thu 30/10/25	Thu 30/10/25	BUCO
24	3.7 Cut and remove area of asphalt on grid line 1 for plumbing works	1 day	Wed 29/10/25	Wed 29/10/25	COMPLETE CONCRETE CUTTING/BUCO

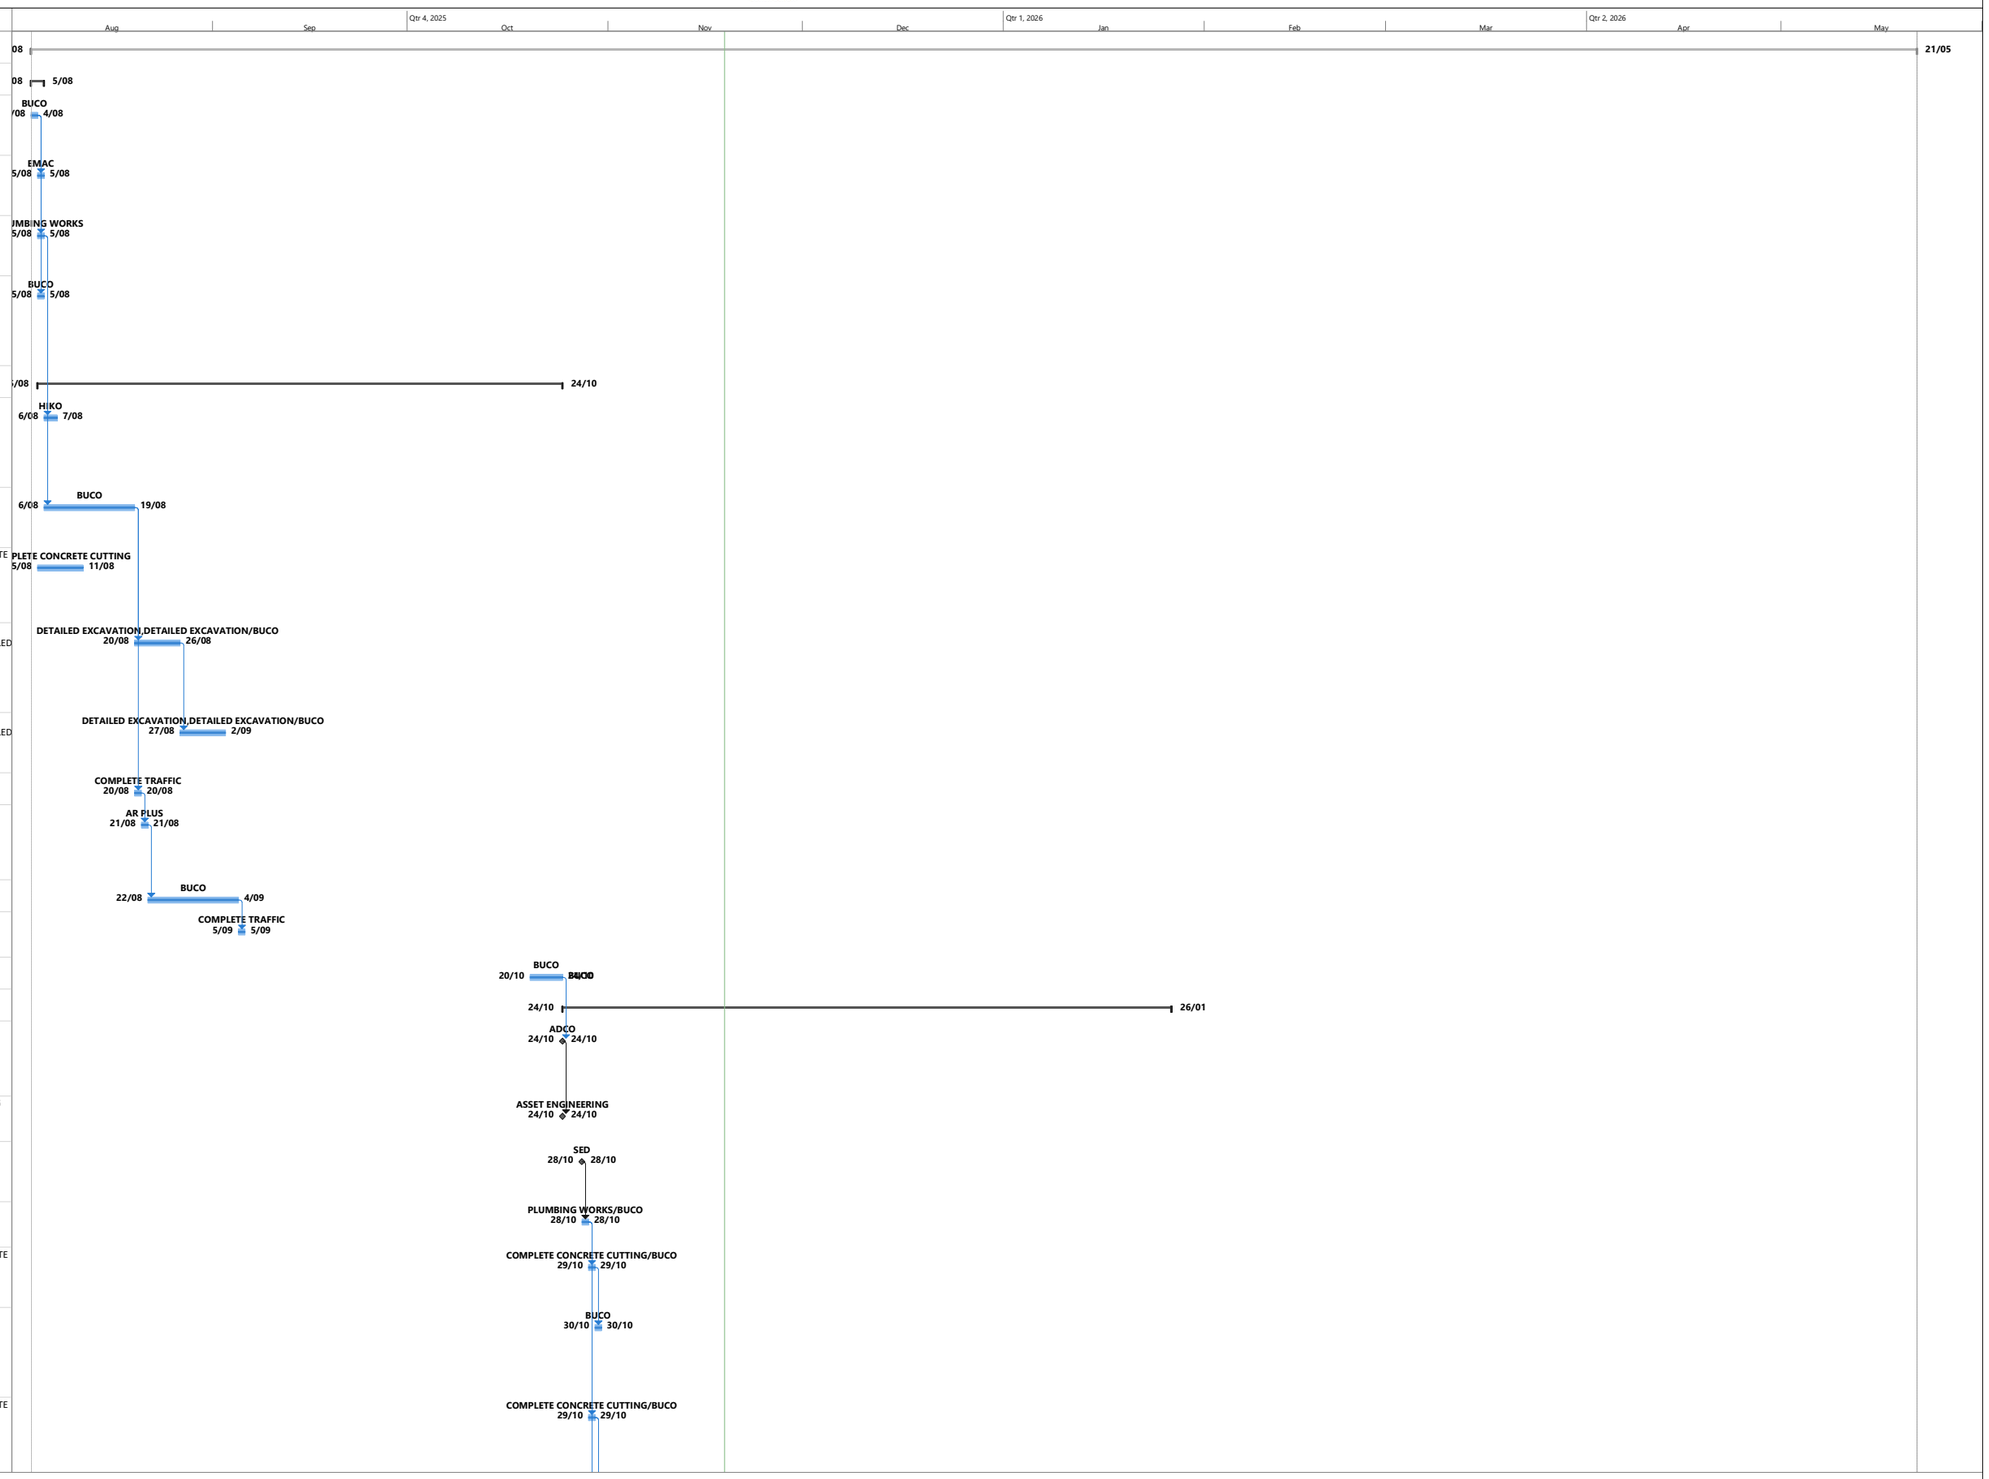

ID	Task Name	Duration	Start	Finish	Resource Names
25	3.8 Baylocate scanning around TCC manhole to confirm if there are any services running underneath to allow manhole to drop in height	0.5 days	Thu 30/10/25	Thu 30/10/25	BAYLOCATE
26	3.9 expose TCC manhole and services for plumbing works	1 day	Thu 30/10/25	Thu 30/10/25	PLUMBING WORKS
27	3.10 Remove joinery in the front entry to allow for excavation on street within hoarding	0.5 days	Wed 29/10/25	Wed 29/10/25	BUCO
28	3.11 Install hoarding from grid line A-B for the removal of existing wall and to allow constrution of new concrete filled block wall and grid line 1 where door to cameron road has been removed	1.5 days	Wed 29/10/25	Thu 30/10/25	BUCO
29	3.12 Run new plumbing services through chase in floor	3 days	Fri 31/10/25	Tue 4/11/25	PLUMBING WORKS
30	3.13 Remove existing wall on grid line A-B	2 days	Fri 31/10/25	Mon 3/11/25	BUCO
31	3.14 Install DPM, reinforcing and waterbars to all requried areas	4 days	Fri 31/10/25	Wed 5/11/25	BUCO
32	3.15 Pre Pour Inspection	0 days	Thu 6/11/25	Thu 6/11/25	TCC
33	3.16 Pour concrete to all required areas in floor	1 day	Thu 6/11/25	Thu 6/11/25	BUCO
34	3.17 Allowance to repair any footpaths or kerbing if needed	3 days	Fri 7/11/25	Tue 11/11/25	BUCO
35	3.18 Replace existing purlins where new roof mount system is to be installed	1 day	Fri 7/11/25	Fri 7/11/25	BUCO
36	3.19 Install new block wall from grid A-B	5 days	Mon 10/11/25	Fri 14/11/25	CITY BRICK
37	3.20 Blockwork inspection	0 days	Fri 14/11/25	Fri 14/11/25	TCC
38	3.21 Pour concrete to new block wall between grid lines A-B (to be cmopleted over 2 concrete pours)	2 days	Mon 17/11/25	Tue 18/11/25	CITY BRICK
39	3.22 Set up Scaffolding/edge protection for gutter and re-roof	3 days	Mon 10/11/25	Wed 12/11/25	VERGE/BUCO/ADCO
40	3.23 Install new pc aluminium gutter insert and replace existing roofing iron	10 days	Thu 13/11/25	Wed 26/11/25	ADCO
41	3.24 Install new roof mount system for HVAC/AC units	1 day	Mon 19/01/26	Mon 19/01/26	HIKO
42	3.25 Install new HVAC/AC system on mounting system	5 days	Tue 20/01/26	Mon 26/01/26	HIKO
43	3.26 Install new colour steel cap flashing	2 days	Thu 27/11/25	Fri 28/11/25	ADCO
44	3.27 Install propping to existing purlins between grid line A+B to allow for façade demolition	2 days	Tue 18/11/25	Wed 19/11/25	VERGE

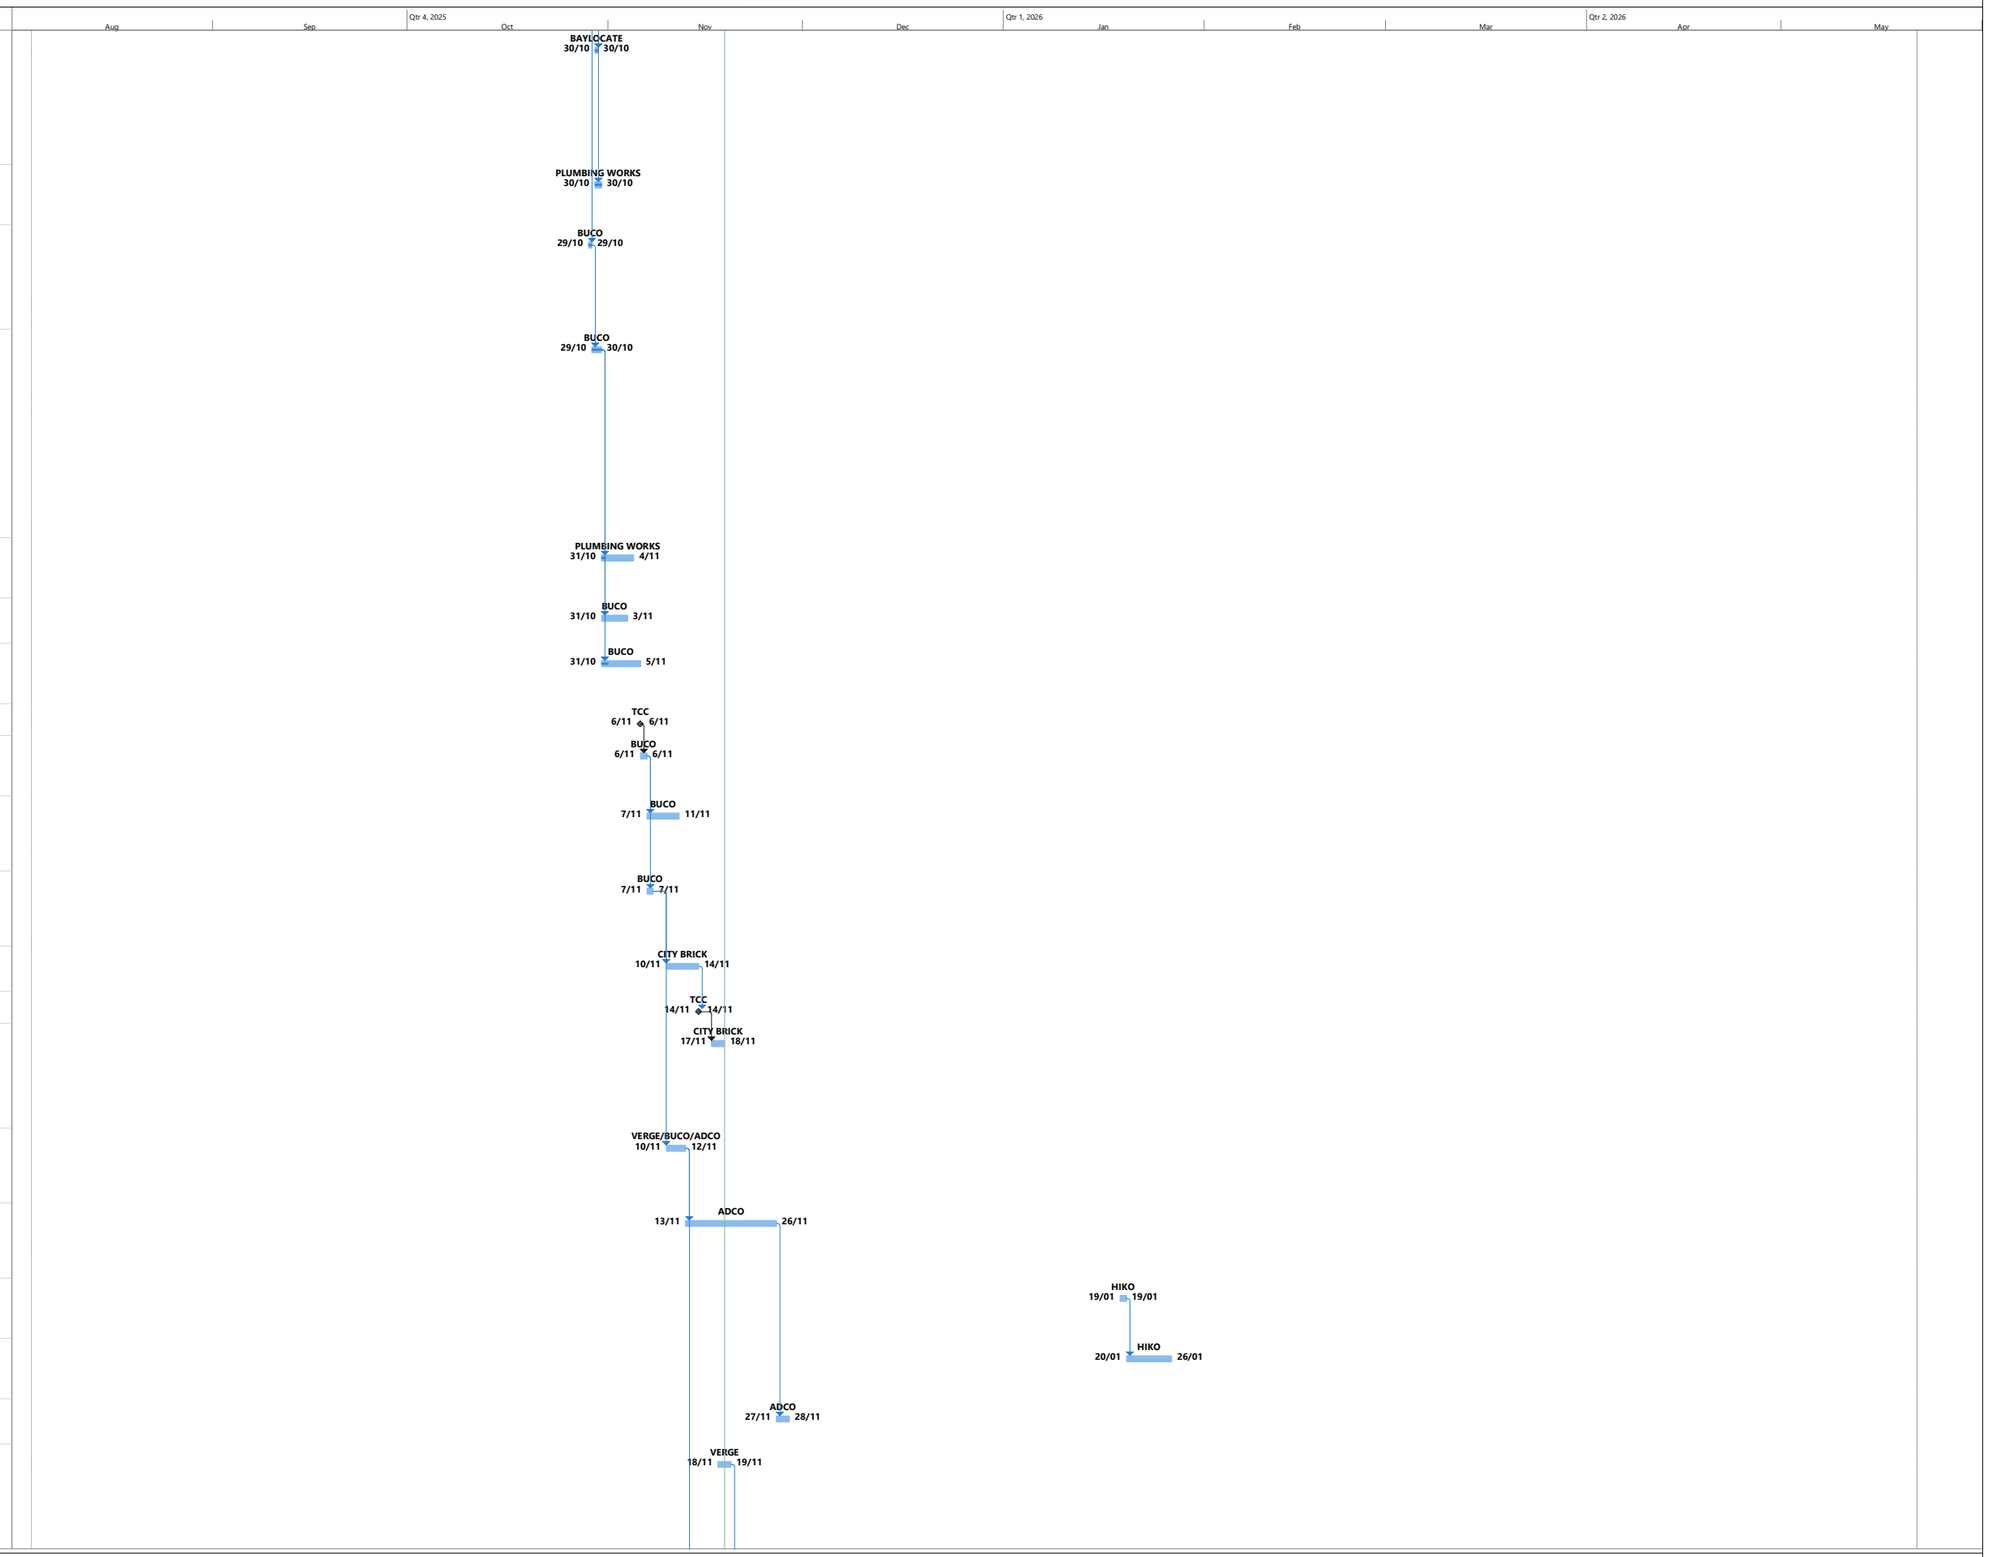

ID	Task Name	Duration	Start	Finish	Resource Names
45	3.28 Remove façade framing and structure to allow for new steel portal on grid line 1	7 days	Thu 20/11/25	Fri 28/11/25	BUCO
46	3.29 Install structural steel portal to grid line 1	3 days	Mon 1/12/25	Wed 3/12/25	ASSET ENGINEERING
47	3.30 Install propping to all existing steel trusses for structural steel install	5 days	Mon 15/12/25	Fri 19/12/25	VERGE
48	3.31 Install new structural steel to walls and roof structure inclusive of all bracing	20 days	Mon 22/12/25	Fri 16/01/26	ASSET ENGINEERING
49	**4 Construction**	**133 days**	**Thu 13/11/25**	**Thu 21/05/26**	
50	4.1 ASBESTOS REMOVAL company to remove all cladding and asbestos to the rear gable NIGHT WORKS	1 day	Thu 13/11/25	Thu 13/11/25	AR PLUS
51	4.2 Framing remedials where required to rear gable post asbestos removal	1 day	Thu 13/11/25	Thu 13/11/25	BUCO
52	4.3 Install new building paper and 20mm cavity battens to rear gable	2 days	Fri 14/11/25	Mon 17/11/25	BUCO
53	4.4 Framing/pre wrap inspection	0 days	Mon 17/11/25	Mon 17/11/25	TCC
54	4.5 Post wrap/cavity inspection	0 days	Mon 17/11/25	Mon 17/11/25	TCC
55	4.6 Install new James Hardie AXON panel cladding to the rear gable over laneway	4 days	Tue 18/11/25	Fri 21/11/25	BUCO
56	4.7 Paint new James Hardie AXON panel to match roof colour	3 days	Mon 24/11/25	Wed 26/11/25	PRM
57	4.8 Remove scaffolding and TMP to laneway	1 day	Thu 27/11/25	Thu 27/11/25	VERGE
58	4.9 Install new 140x90 framing to façade and steel portal on grid line 1	4 days	Thu 4/12/25	Tue 9/12/25	BUCO
59	4.10 Install new building wrap to façade framing	1 day	Wed 10/12/25	Wed 10/12/25	BUCO
60	4.11 Install new timber framing, 190x45 purlins and roof framing over new canopy	3 days	Thu 11/12/25	Mon 15/12/25	BUCO
61	4.12 Install new pc aluminium gutter to canopy with all appropriate flashings, stops ends and outlets	1 day	Mon 19/01/26	Mon 19/01/26	ADCO
62	4.13 Install new building paper and new roofing iron to canopy framing	1 day	Tue 20/01/26	Tue 20/01/26	ACDO
63	4.14 Install new metal sheet cladding to façade on street elevation with appropriate flashings to roofing	5 days	Wed 21/01/26	Tue 27/01/26	ADCO
64	4.15 Install new soffit cladding to canopy	2 days	Wed 28/01/26	Thu 29/01/26	BUCO
65	4.16 Remove and replace all aluminium joinery to exterior where required	9 days	Fri 30/01/26	Thu 12/02/26	BUCO/TASMAN ALUMINIUM

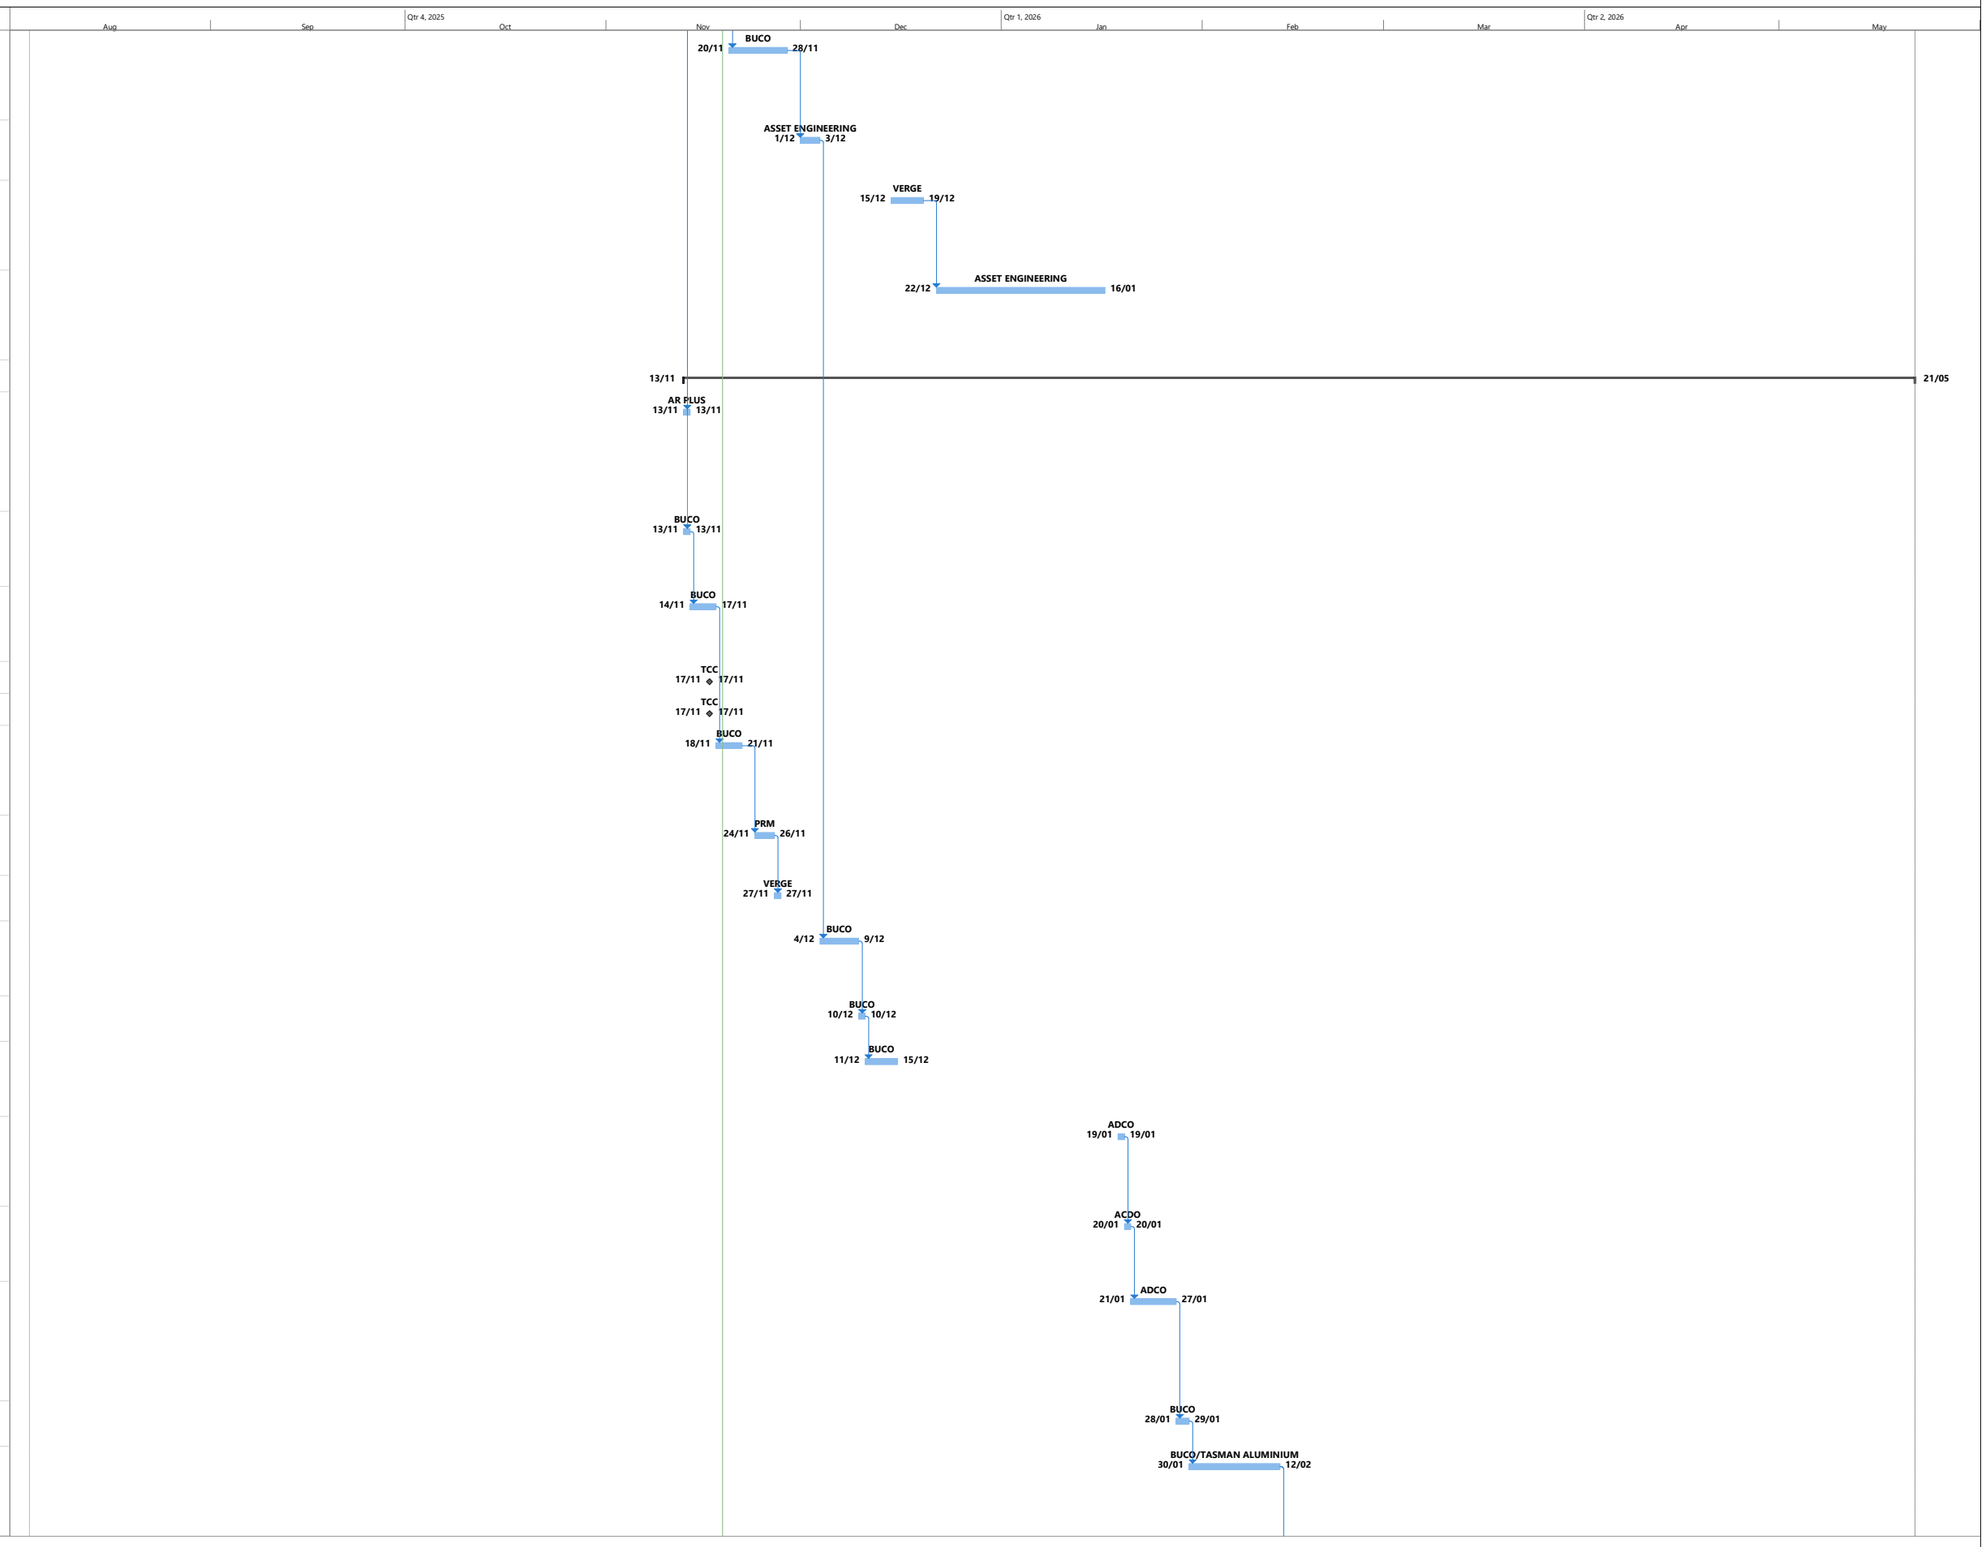
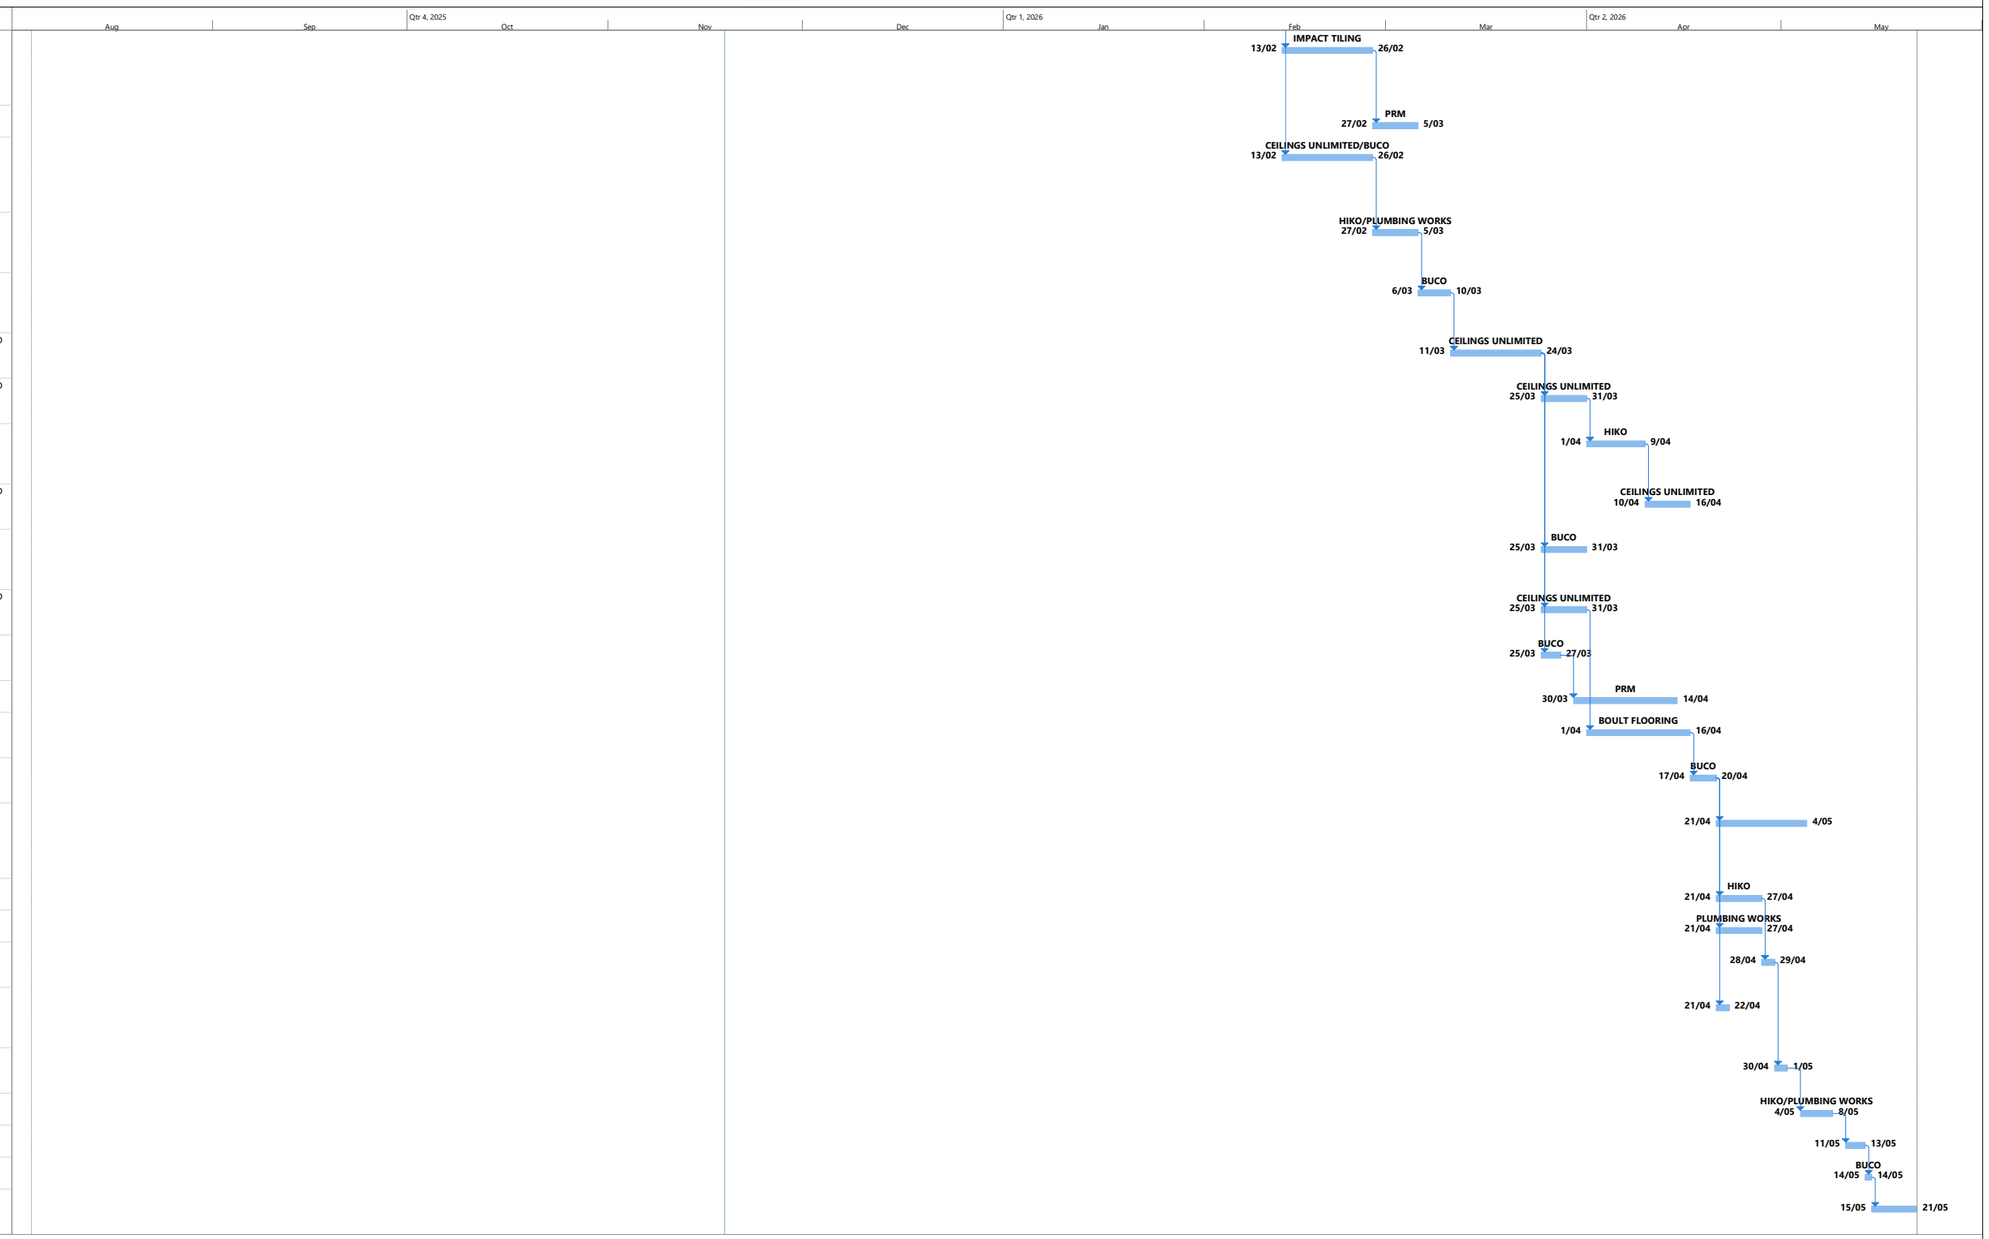
ID	Task Name	Duration	Start	Finish	Resource Names
66	4.17 Install new tile cladding to façade and wall to southern elevation	10 days	Fri 13/02/26	Thu 26/02/26	IMPACT TILING
67	4.18 Paint exterior of building	5 days	Fri 27/02/26	Thu 5/03/26	PRM
68	4.19 Install all new internal wall framing and strapping to external walls	10 days	Fri 13/02/26	Thu 26/02/26	CEILINGS UNLIMITED/BUCO
69	4.20 Run all new services through walls where required	5 days	Fri 27/02/26	Thu 5/03/26	HIKO/PLUMBING WORKS
70	4.21 Install Acoustic insulation where required	3 days	Fri 6/03/26	Tue 10/03/26	BUCO
71	4.22 Install new wall linings throughout	10 days	Wed 11/03/26	Tue 24/03/26	CEILINGS UNLIMITED
72	4.23 Install new ceiling grid throughout	5 days	Wed 25/03/26	Tue 31/03/26	CEILINGS UNLIMITED
73	4.24 Run services through ceiling grid where required	5 days	Wed 1/04/26	Thu 9/04/26	HIKO
74	4.25 Install new ceiling tiles throughout	5 days	Fri 10/04/26	Thu 16/04/26	CEILINGS UNLIMITED
75	4.26 install all new internal doors and windows	5 days	Wed 25/03/26	Tue 31/03/26	BUCO
76	4.27 Plaster all new wall and ceiling linings	5 days	Wed 25/03/26	Tue 31/03/26	CEILINGS UNLIMITED
77	4.28 Install all trims and finishing lines	3 days	Wed 25/03/26	Fri 27/03/26	BUCO
78	4.29 Interior painting	10 days	Mon 30/03/26	Tue 14/04/26	PRM
79	4.30 Install all new floor linings throughout	10 days	Wed 1/04/26	Thu 16/04/26	BOULT FLOORING
80	4.31 Install flooring protection throughout	2 days	Fri 17/04/26	Mon 20/04/26	BUCO
81	4.32 Install all new cabinetry to café, boardroom, reception and meeting rooms	10 days	Tue 21/04/26	Mon 4/05/26	
82	4.33 Electrical fitoff	5 days	Tue 21/04/26	Mon 27/04/26	HIKO
83	4.34 Plumbing final fitoff	5 days	Tue 21/04/26	Mon 27/04/26	PLUMBING WORKS
84	4.35 Install all required signage throughout	2 days	Tue 28/04/26	Wed 29/04/26	
85	4.36 Install all required hardware throughout	2 days	Tue 21/04/26	Wed 22/04/26	
86	4.37 Install any signage required by client/tenant	2 days	Thu 30/04/26	Fri 1/05/26	
87	4.38 Commissioning	5 days	Mon 4/05/26	Fri 8/05/26	HIKO/PLUMBING WORKS
88	4.39 Commercial clean	3 days	Mon 11/05/26	Wed 13/05/26	
89	4.40 Final QA	1 day	Thu 14/05/26	Thu 14/05/26	BUCO
90	4.41 Time allowance for snags	5 days	Fri 15/05/26	Thu 21/05/26
