PAPAMOA PLAZA STAGE 3

Construction Programme Rev 01 - Date 17102025

Post Contract Execution

Naylor Love

TINLINE

0%	PAPAMOA PLAZA STAGE 3	781 days	Wed 15/01/25	Fri 31/07/26
0%	MILESTONES	261 days	Wed 12/02/25	Fri 31/07/26
100%	Milestone: Contract Award to Naylor Love	0 days	Wed 8/10/25	Wed 8/10/25
100%	Milestone: Develop Design Complete	0 days	Mon 30/06/25	Mon 30/06/25
100%	Milestone: Site Establishment	0 days	Wed 27/08/25	Wed 27/08/25
100%	Milestone: Detailed design complete Stage1	0 days	Wed 12/02/25	Wed 12/02/25
100%	Milestone: BC1 Lodgement	0 days	Wed 12/02/25	Wed 12/02/25
100%	Milestone: BC1 Uplifted	0 days	Tue 15/04/25	Tue 15/04/25
100%	Milestone: Detailed design complete Stage2	0 days	Mon 23/06/25	Mon 23/06/25
100%	Milestone: BC2 Lodgement	0 days	Wed 25/06/25	Wed 25/06/25
100%	Milestone: BC2 Uplifted	0 days	Thu 4/09/25	Thu 4/09/25
100%	Milestone: Detailed design complete Stage3	0 days	Mon 18/08/25	Mon 18/08/25
100%	Milestone: BC 3 Lodgement	0 days	Tue 2/09/25	Tue 2/09/25
0%	Milestone: BC3 Uplifted	0 days	Mon 3/11/25	Mon 3/11/25
100%	Milestone: Construction Commencement	0 days	Mon 21/07/25	Mon 21/07/25
0%	Milestone: Building Watertight	0 days	Mon 15/06/26	Mon 15/06/26
0%	Milestone: Client Fit Out Access	0 days	Mon 15/06/26	Mon 15/06/26
0%	Milestone: Practical Completion (Contract)	0 days	Fri 31/07/26	Fri 31/07/26
96%	CONTRACT	684 days	Wed 15/01/25	Wed 8/10/25
82%	STAGED BUILDING CONSENT	538 days	Wed 12/02/25	Mon 16/11/26
100%	BC Stage 1 - DW - Council services relocation	50 days	Wed 12/02/25	Thu 24/04/25
100%	BC Stage 1: Pre-lodgement meeting TCC	1 day	Wed 12/02/25	Wed 12/02/25
100%	BC Stage 1: BC - Development works issued	1 day	Tue 15/04/25	Tue 15/04/25
100%	BC Stage 1: BC Documents Revised for IFC	5 days	Wed 16/04/25	Thu 24/04/25
100%	BC Stage 2 - Civils - Foundations & Structural	44 days	Fri 6/06/25	Fri 24/08/25
100%	BC Stage 2: Complete - Struct Design	20 days	Fri 6/06/25	Mon 23/06/25
100%	BC Stage 2: Pre-lodgement meeting TCC	1 day	Tue 24/06/25	Tue 24/06/25
100%	BC Stage 2: Lodge BC documents	1 day	Wed 25/06/25	Wed 25/06/25
100%	BC Stage 2: Building BC processing (estimate)	20 days	Thu 26/06/25	Wed 23/07/25
100%	BC Stage 2: Building RFI process (Prov time)	5 days	Thu 24/07/25	Wed 30/07/25
100%	BC Stage 2: Building BC issued	1 day	Thu 4/09/25	Thu 4/09/25
100%	BC Stage 2: BC Documents Revised for IFC	7 days	Thu 18/08/25	Fri 26/09/25
67%	BC Stage 3 - Architectural	99 days	Tue 24/06/25	Mon 10/11/25
100%	Façade selection - Option 05	0 days	Wed 16/07/25	Wed 16/07/25
100%	BC Stage 3: Complete - Arch Design	50 days	Tue 24/06/25	Mon 1/09/25
100%	BC Stage 3: Complete review of Fire report	5 days	Tue 12/08/25	Mon 18/08/25
100%	BC Stage 3: Pre-lodgement meeting TCC	1 day	Tue 19/08/25	Tue 19/08/25
100%	BC Stage 3: Lodge BC documents	1 day	Tue 2/09/25	Tue 2/09/25
100%	BC Stage 3: Building BC processing (estimate)	20 days	Wed 3/09/25	Tue 30/09/25
50%	BC Stage 3: Building RFI process (prov time)	14 days	Mon 12/10/25	Fri 31/10/25
0%	BC Stage 3: Building BC issued	1 day	Mon 3/11/25	Mon 3/11/25
0%	BC Stage 3: BC Documents Revised for IFC	5 days	Tue 4/11/25	Mon 10/11/25
15%	PRE-CONSTRUCTION AND PROCUREMENT	194 days	Tue 22/07/25	Thu 7/05/26
26%	Procurement	194 days	Tue 22/07/25	Thu 7/05/26
27%	Structural Steel	101 days	Mon 11/08/25	Mon 12/01/26
100%	Proc: SS: Subcontractor engagement	13 days	Mon 11/08/25	Wed 27/08/25
100%	Proc: SS: Confirm steel quantities	3 days	Mon 25/08/25	Wed 27/08/25
100%	Proc: SS: Steel order	25 days	Wed 27/08/25	Tue 30/09/25
0%	Proc: SS: Shop drawing production A-E	12 days	Fri 12/09/25	Tue 3/12/25
50%	Proc: SS: Shop drawing production	20 days	Fri 12/09/25	Thu 23/10/25
0%	Proc: SS: Subcontractor RFI process	5 days	Tue 21/10/25	Tue 28/10/25
0%	Proc: SS: Shop drawing review	5 days	Tue 21/10/25	Tue 28/10/25
0%	Proc: SS: Fabrication drawings	5 days	Wed 29/10/25	Tue 4/11/25
0%	Proc: SS: Fabrication & paint GL A - F	30 days	Wed 29/10/25	Tue 9/12/25
0%	Proc: SS: Shop drawing production F-O	77 days	Fri 12/09/25	Mon 12/01/26
0%	Proc: SS: Shop drawing production	40 days	Fri 12/09/25	Fri 7/11/25
0%	Proc: SS: Subcontractor RFI process	5 days	Wed 5/11/25	Tue 11/11/25
0%	Proc: SS: Shop drawing review	5 days	Wed 5/11/25	Tue 11/11/25
0%	Proc: SS: Fabrication drawings	5 days	Wed 12/11/25	Tue 18/11/25
0%	Proc: SS: Fabrication & paint GL F-O	35 days	Wed 12/11/25	Mon 12/01/26
0%	Shopfront Glazing	130 days	Mon 20/10/25	Thu 7/05/26
0%	Proc: Glazing: Subcontractor engagement	5 days	Mon 20/10/25	Fri 24/10/25
0%	Proc: Glazing: Shop drawing	30 days	Tue 11/11/25	Mon 22/12/25
0%	Proc: Glazing: Shop drawing review	10 days	Tue 22/12/25	Fri 16/01/26
0%	Proc: Glazing: Shop drawing revision	10 days	Mon 19/01/26	Fri 30/01/26
0%	Proc: Glazing: Shop drawing rev. review	5 days	Mon 2/02/26	Mon 9/02/26
0%	Proc: Glazing: Fabrication drawings	10 days	Tue 10/02/26	Mon 23/02/26
0%	Proc: Glazing: Frame material order	15 days	Tue 26/12/25	Fri 23/01/26
0%	Proc: Glazing: Frame production	40 days	Tue 24/02/26	Wed 22/04/26
0%	Proc: Glazing: Glass order	50 days	Tue 24/02/26	Thu 7/05/26
100%	Civil	18 days	Tue 22/07/25	Thu 14/08/25
100%	Proc: Civil: Subcontractor engagement	7 days	Tue 22/07/25	Wed 30/07/25
100%	Proc: Civil: Subcontractor mobilisation	5 days	Fri 1/08/25	Thu 7/08/25
100%	Proc: Civil: Material order	5 days	Fri 8/08/25	Thu 14/08/25
0%	Roof panels	75 days	Tue 28/10/25	Mon 23/02/26
50%	Roof panels: Subcontractor engagement	5 days	Tue 28/10/25	Mon 3/11/25
0%	Roof panels: Shop drawing production	20 days	Tue 4/11/25	Mon 1/12/25
0%	Roof panels: Shop drawing review	5 days	Tue 2/12/25	Mon 8/12/25
0%	Roof panels: Shop drawing IFC	5 days	Tue 9/12/25	Mon 15/12/25
0%	Roof panels: Production	40 days	Tue 16/12/25	Mon 23/02/26
12%	CONSTRUCTION	244 days	Mon 21/07/25	Fri 17/07/26
100%	Enabling Works	28 days	Mon 21/07/25	Wed 27/08/25
100%	Enabling: Site establishment	5 days	Mon 21/07/25	Fri 25/07/25
100%	Enabling: GRS ex. Services	5 days	Thu 24/07/25	Wed 30/07/25
100%	Enabling: Temporary services	20 days	Thu 31/07/25	Wed 27/08/25
100%	Enabling: Sediment control	2 days	Tue 26/07/25	Wed 30/07/25
42%	Civil	182 days	Mon 4/08/25	Tue 5/05/26
100%	Civil: SW drainage (Sth/West - Council)	24 days	Mon 25/08/25	Thu 25/09/25
100%	Civil: WW drainage (Council)	15 days	Mon 4/08/25	Fri 22/08/25
0%	Civil: SW drainage (west - Private)	5 days	Tue 14/04/26	Mon 20/04/26
0%	Civil: SW drainage (east - Private)	10 days	Tue 21/04/26	Tue 5/05/26
38%	Foundations	83 days	Fri 10/08/25	Tue 27/01/26
38%	Foundations Phase 1 GL A - F	66 days	Fri 10/08/25	Mon 24/11/25
70%	Civils: Cut and fill (provisional)	12 days	Fri 10/08/25	Mon 6/10/25
70%	Civils: Soft spots - (provisional)	10 days	Tue 7/10/25	Mon 20/10/25
35%	Founds: Phase 1: FRP Raft Foundation	8 days	Tue 14/10/25	Thu 23/10/25
0%	Founds: Column Plinth & Slab edge	7 days	Fri 24/10/25	Tue 4/11/25
0%	Founds: Phase 1: Prep Blinding, Slab & Beams	4 days	Wed 5/11/25	Mon 10/11/25
0%	Founds: Phase 1: SS Drainage	2 days	Mon 10/11/25	Tue 11/11/25
0%	Founds: Phase 1: DPM	1 day	Wed 12/11/25	Wed 12/11/25
0%	Founds: Phase 1: FRP tie beams	2 days	Wed 12/11/25	Thu 13/11/25
0%	Founds: Phase 1: Construction joint x2	3 days	Fri 14/11/25	Tue 18/11/25
0%	Founds: Phase 1: Slab Reo	3 days	Tue 18/11/25	Thu 20/11/25
0%	Founds: Phase 1: Pour Slab	1 day	Fri 21/11/25	Fri 21/11/25
0%	Founds: Phase 1: Saw Cuts	1 day	Mon 24/11/25	Mon 24/11/25
0%	Foundations Phase 2 GL F - I	22 days	Wed 5/11/25	Thu 4/12/25
0%	Founds: Phase 2: FRP Raft Foundation	6 days	Wed 5/11/25	Wed 12/11/25
0%	Founds: Column Plinth & Slab edge	4 days	Thu 13/11/25	Tue 18/11/25
0%	Founds: Phase 2: Prep Blinding, Slab & Beams	4 days	Wed 19/11/25	Fri 21/11/25
0%	Founds: Phase 2: SS Drainage	2 days	Mon 24/11/25	Tue 25/11/25
0%	Founds: Phase 2: DPM	1 day	Wed 26/11/25	Wed 26/11/25
0%	Founds: Phase 2: FRP tie beams	2 days	Wed 26/11/25	Thu 27/11/25
0%	Founds: Phase 2: Construction joint	2 days	Fri 28/11/25	Mon 1/12/25
0%	Founds: Phase 2: Slab Reo	2 days	Mon 1/12/25	Tue 2/12/25
0%	Founds: Phase 2: Pour Slab	1 day	Wed 3/12/25	Wed 3/12/25
0%	Founds: Phase 2: Saw Cuts	1 day	Thu 4/12/25	Thu 4/12/25
0%	Foundations Phase 3 GL I - L	21 days	Wed 30/12/25	Tue 27/01/26
0%	Founds: Phase 3: FRP Raft Foundation	6 days	Wed 30/12/25	Wed 26/12/25
0%	Founds: Column Plinth & Slab edge	4 days	Thu 27/12/25	Tue 2/12/25
0%	Founds: Phase 3: Prep Blinding, Slab & Beams	4 days	Wed 3/12/25	Fri 5/12/25
0%	Founds: Phase 3: SS Drainage Pet Stock	5 days	Mon 8/12/25	Fri 12/12/25

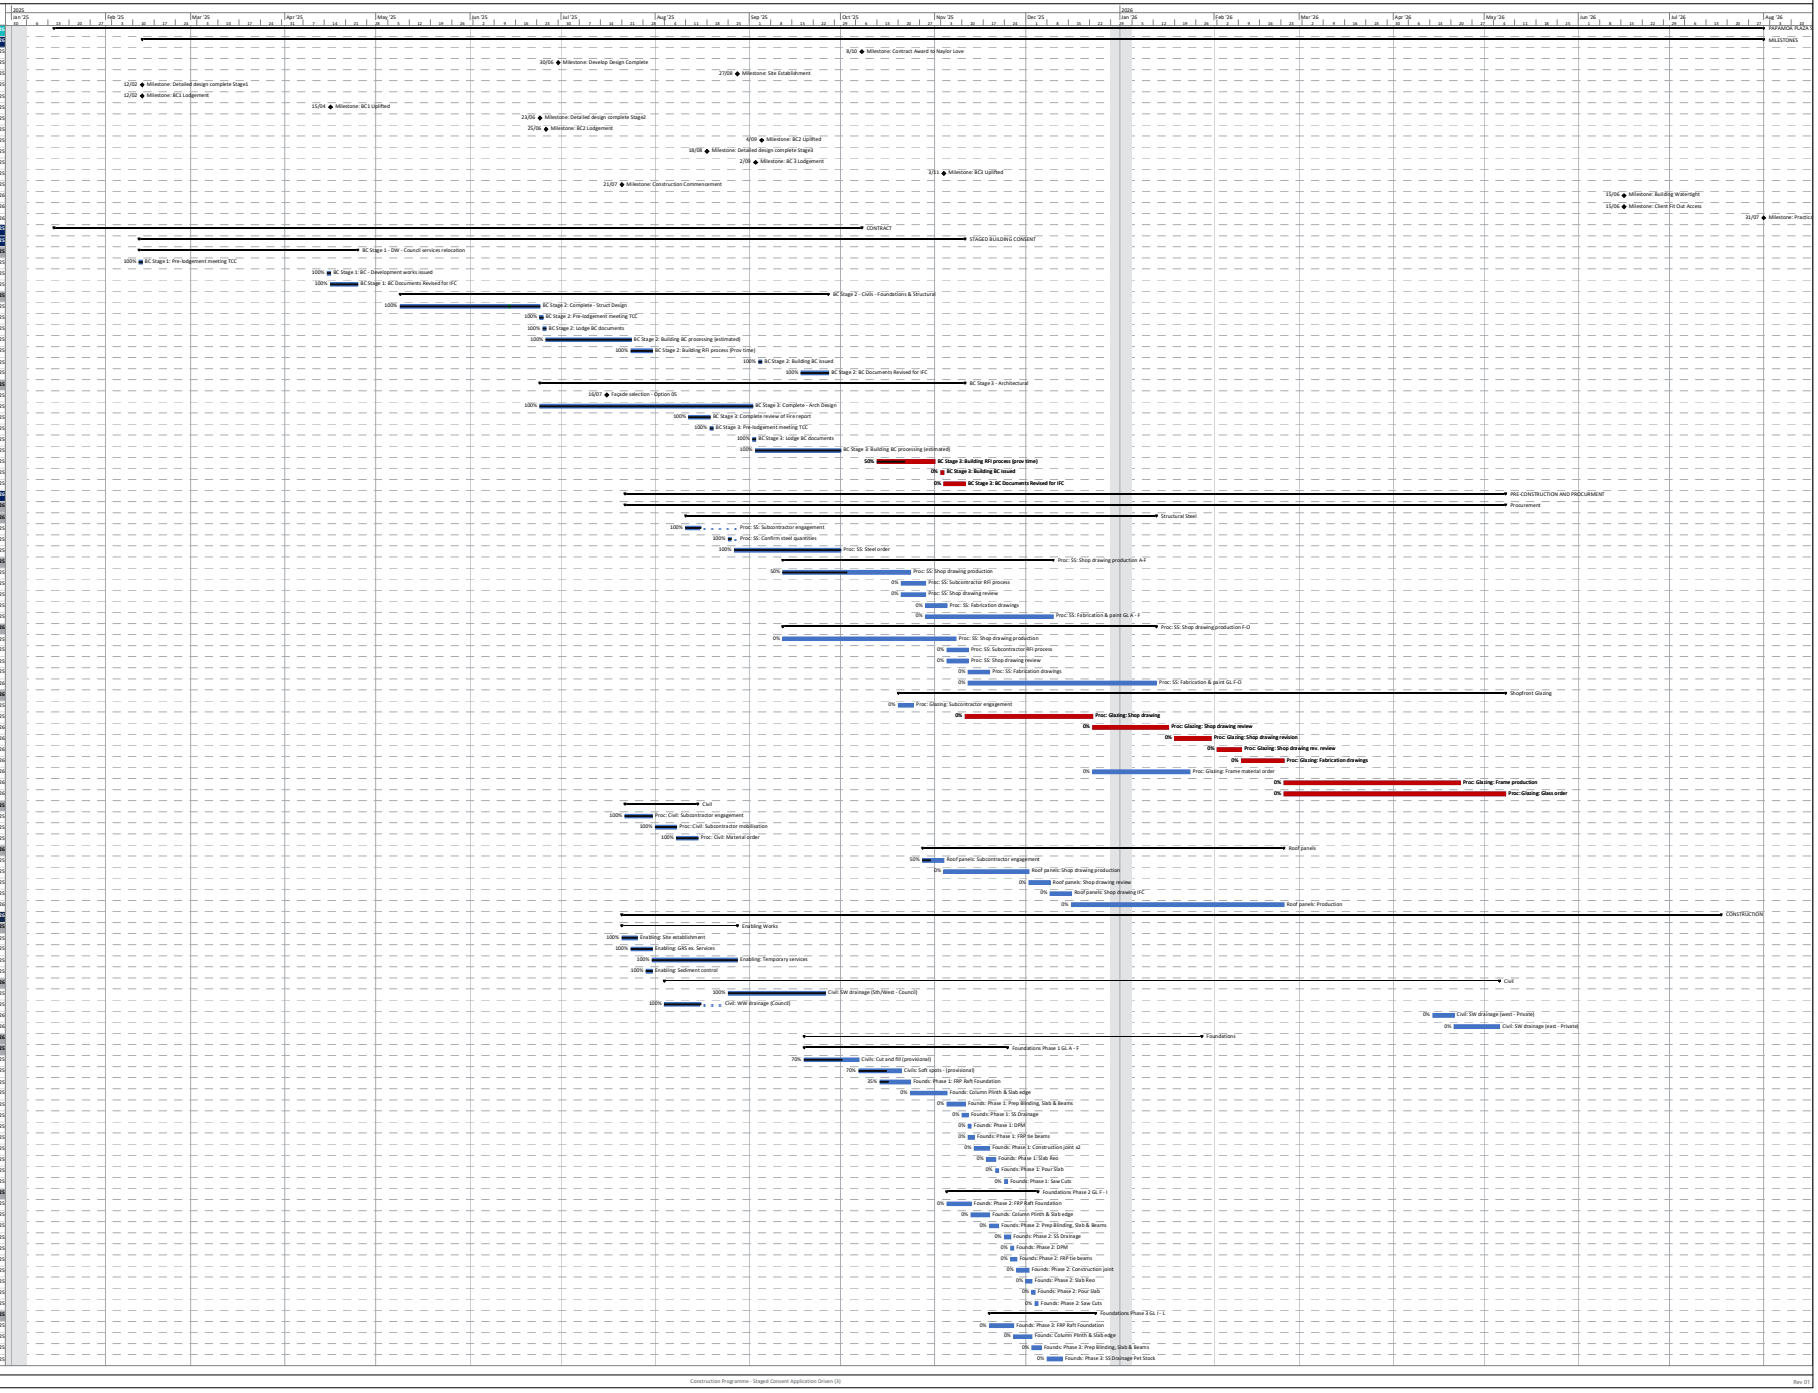

PAPAMOA PLAZA STAGE 3

Construction Programme Rev 01 - Date 17102025

Post Contract Execution
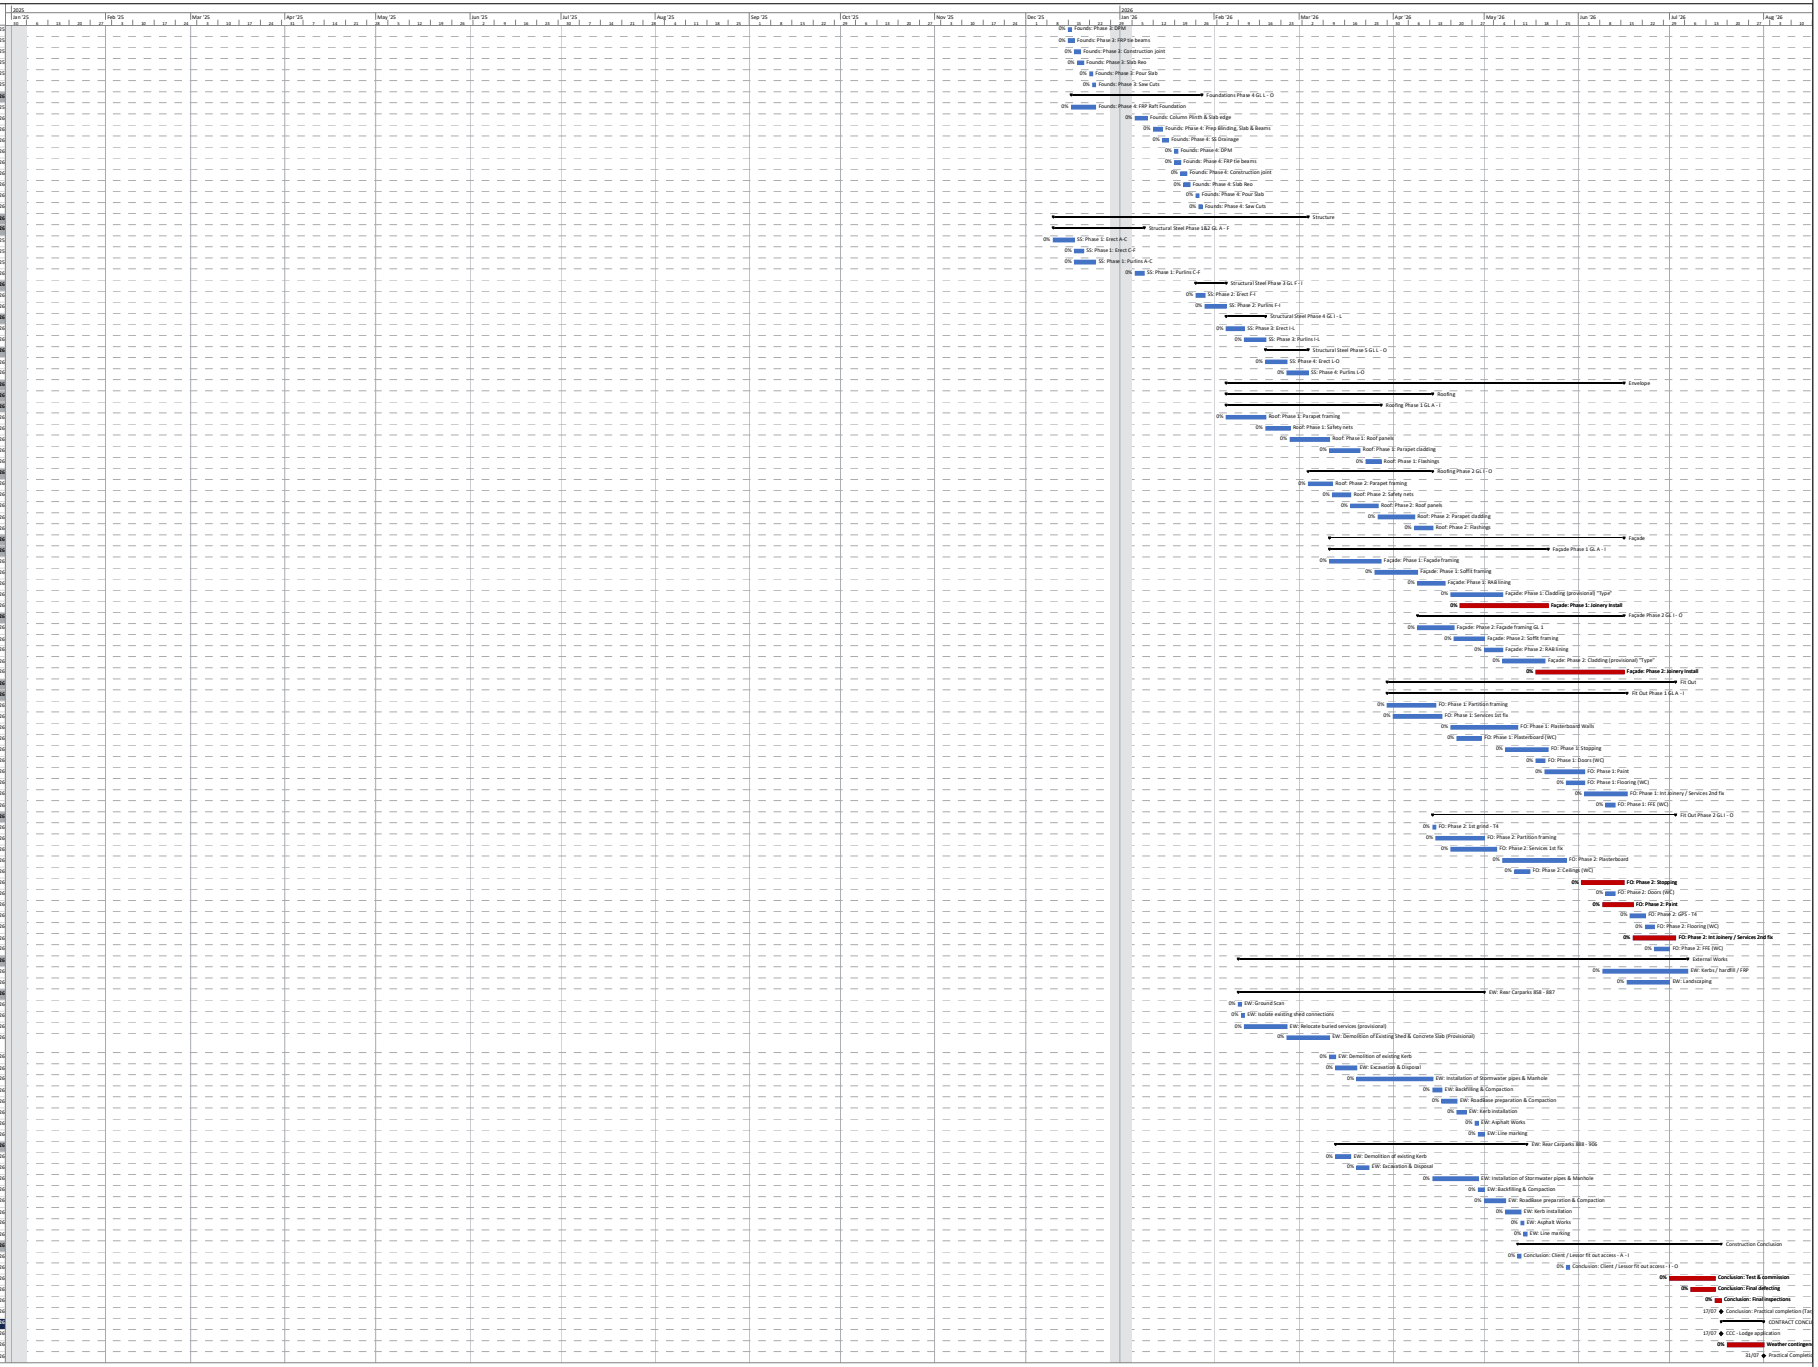
0%	Founds: Phase 3: DPM	1 day	Mon 15/12/25	Mon 15/12/25
0%	Founds: Phase 3: FRP tie beams	2 days	Mon 15/12/25	Tue 16/12/25
0%	Founds: Phase 3: Construction joint	2 days	Wed 17/12/25	Thu 18/12/25
0%	Founds: Phase 3: Slab Reo	2 days	Thu 18/12/25	Fri 19/12/25
0%	Founds: Phase 3: Pour Slab	1 day	Mon 22/12/25	Mon 22/12/25
0%	Founds: Phase 3: Saw Cuts	1 day	Tue 23/12/25	Tue 23/12/25
0%	**Foundations Phase 4 GL L - O**	**22 days**	**Tue 16/12/25**	**Tue 27/01/26**
0%	Founds: Phase 4: FRP Raft Foundation	6 days	Tue 16/12/25	Tue 23/12/25
0%	Founds: Column Plinth & Slab edge	4 days	Tue 6/01/26	Fri 9/01/26
0%	Founds: Phase 4: Prep Blinding, Slab & Be	3 days	Mon 12/01/26	Wed 14/01/26
0%	Founds: Phase 4: SS Drainage	2 days	Thu 15/01/26	Fri 16/01/26
0%	Founds: Phase 4: DPM	1 day	Mon 19/01/26	Mon 19/01/26
0%	Founds: Phase 4: FRP tie beams	2 days	Mon 19/01/26	Tue 20/01/26
0%	Founds: Phase 4: Construction joint	2 days	Wed 21/01/26	Thu 22/01/26
0%	Founds: Phase 4: Slab Reo	2 days	Thu 22/01/26	Fri 23/01/26
0%	Founds: Phase 4: Pour Slab	1 day	Mon 26/01/26	Mon 26/01/26
0%	Founds: Phase 4: Saw Cuts	1 day	Tue 27/01/26	Tue 27/01/26
0%	**Structure**	**10 days**	**Wed 10/12/25**	**Tue 3/03/26**
0%	**Structural Steel Phase 1&2 GL A - F**	**13 days**	**Wed 10/12/25**	**Thu 8/01/26**
0%	SS: Phase 1: Erect A-C	5 days	Wed 10/12/25	Tue 16/12/25
0%	SS: Phase 1: Erect C-F	3 days	Wed 17/12/25	Fri 19/12/25
0%	SS: Phase 1: Purlins A-C	5 days	Wed 17/12/25	Tue 23/12/25
0%	SS: Phase 1: Purlins C-F	3 days	Tue 6/01/26	Thu 8/01/26
0%	**Structural Steel Phase 3 GL F - I**	**8 days**	**Mon 26/01/26**	**Wed 4/02/26**
0%	SS: Phase 2: Erect F-I	3 days	Mon 26/01/26	Wed 28/01/26
0%	SS: Phase 2: Purlins F-I	5 days	Thu 29/01/26	Wed 4/02/26
0%	**Structural Steel Phase 4 GL I - L**	**6 days**	**Thu 5/02/26**	**Tue 17/02/26**
0%	SS: Phase 3: Erect I-L	3 days	Thu 5/02/26	Tue 10/02/26
0%	SS: Phase 3: Purlins I-L	5 days	Wed 11/02/26	Tue 17/02/26
0%	**Structural Steel Phase 5 GL L - O**	**10 days**	**Wed 18/02/26**	**Tue 3/03/26**
0%	SS: Phase 4: Erect L-O	5 days	Wed 18/02/26	Tue 24/02/26
0%	SS: Phase 4: Purlins L-O	5 days	Wed 25/02/26	Tue 3/03/26
0%	**Envelope**	**88 days**	**Thu 5/02/26**	**Mon 15/06/26**
0%	**Roofing**	**45 days**	**Thu 5/02/26**	**Mon 13/04/26**
0%	**Roofing Phase 1 GL A - I**	**34 days**	**Thu 5/02/26**	**Fri 27/03/26**
0%	Roof: Phase 1: Parapet framing	8 days	Thu 5/02/26	Tue 17/02/26
0%	Roof: Phase 1: Safety nets	6 days	Wed 18/02/26	Wed 25/02/26
0%	Roof: Phase 1: Roof panels	9 days	Thu 26/02/26	Tue 10/03/26
0%	Roof: Phase 1: Parapet cladding	8 days	Wed 11/03/26	Fri 20/03/26
0%	Roof: Phase 1: Flashings	5 days	Mon 23/03/26	Fri 27/03/26
0%	**Roofing Phase 2 GL I - O**	**27 days**	**Wed 4/03/26**	**Mon 13/04/26**
0%	Roof: Phase 2: Parapet framing	6 days	Wed 4/03/26	Wed 11/03/26
0%	Roof: Phase 2: Safety nets	4 days	Thu 12/03/26	Tue 17/03/26
0%	Roof: Phase 2: Roof panels	7 days	Wed 18/03/26	Thu 26/03/26
0%	Roof: Phase 2: Parapet cladding	6 days	Fri 27/03/26	Tue 7/04/26
0%	Roof: Phase 2: Flashings	4 days	Wed 8/04/26	Mon 13/04/26
0%	**Façade**	**65 days**	**Wed 11/03/26**	**Mon 15/06/26**
0%	**Façade Phase 1 GL A - I**	**49 days**	**Wed 11/03/26**	**Thu 21/05/26**
0%	Façade: Phase 1: Façade framing	13 days	Wed 11/03/26	Fri 27/03/26
0%	Façade: Phase 1: Soffit framing	8 days	Thu 26/03/26	Wed 8/04/26
0%	Façade: Phase 1: RAB lining	7 days	Thu 9/04/26	Fri 17/04/26
0%	Façade: Phase 1: Cladding (provisiona	12 days	Mon 20/04/26	Wed 6/05/26
0%	Façade: Phase 1: Joinery Install	20 days	Thu 23/04/26	Thu 21/05/26
0%	**Façade Phase 2 GL I - O**	**46 days**	**Thu 9/04/26**	**Mon 15/06/26**
0%	Façade: Phase 2: Façade framing GL I	8 days	Thu 9/04/26	Mon 20/04/26
0%	Façade: Phase 2: Soffit framing	7 days	Tue 21/04/26	Thu 30/04/26
0%	Façade: Phase 2: RAB lining	4 days	Fri 1/05/26	Wed 6/05/26
0%	Façade: Phase 2: Cladding (provisiona	10 days	Thu 7/05/26	Wed 20/05/26
0%	Façade: Phase 2: Joinery Install	20 days	Mon 18/05/26	Mon 15/06/26
0%	**Fit Out**	**65 days**	**Mon 30/03/26**	**Thu 2/07/26**
0%	**Fit Out Phase 1 GL A - I**	**13 days**	**Mon 30/03/26**	**Tue 14/04/26**
0%	FO: Phase 1: Partition framing	10 days	Mon 30/03/26	Tue 14/04/26
0%	FO: Phase 1: Services 1st fix	10 days	Wed 1/04/26	Thu 16/04/26
0%	FO: Phase 1: Plasterboard Walls	15 days	Mon 20/04/26	Mon 11/05/26
0%	FO: Phase 1: Plasterboard (WC)	5 days	Wed 22/04/26	Wed 29/04/26
0%	FO: Phase 1: Stopping	10 days	Fri 8/05/26	Thu 21/05/26
0%	FO: Phase 1: Doors (WC)	3 days	Mon 18/05/26	Wed 20/05/26
0%	FO: Phase 1: Paint	8 days	Thu 21/05/26	Tue 2/06/26
0%	FO: Phase 1: Flooring (WC)	3 days	Thu 28/05/26	Tue 2/06/26
0%	FO: Phase 1: Int Joinery / Services 2nd fi	10 days	Wed 3/06/26	Tue 16/06/26
0%	FO: Phase 1: FFE (WC)	3 days	Wed 10/06/26	Fri 12/06/26
0%	**Fit Out Phase 2 GL I - O**	**16 days**	**Tue 14/04/26**	**Thu 2/07/26**
0%	FO: Phase 2: 1st grind - T4	1 day	Tue 14/04/26	Tue 14/04/26
0%	FO: Phase 2: Partition framing	11 days	Wed 15/04/26	Thu 30/04/26
0%	FO: Phase 2: Services 1st fix	10 days	Mon 20/04/26	Mon 4/05/26
0%	FO: Phase 2: Plasterboard	15 days	Thu 7/05/26	Wed 27/05/26
0%	FO: Phase 2: Ceilings (WC)	5 days	Mon 11/05/26	Fri 15/05/26
0%	FO: Phase 2: Stopping	10 days	Tue 2/06/26	Mon 15/06/26
0%	FO: Phase 2: Doors (WC)	3 days	Wed 10/06/26	Fri 12/06/26
0%	FO: Phase 2: Paint	8 days	Tue 9/06/26	Thu 18/06/26
0%	FO: Phase 2: GPS - T4	3 days	Thu 18/06/26	Mon 22/06/26
0%	FO: Phase 2: Flooring (WC)	3 days	Tue 23/06/26	Thu 25/06/26
0%	FO: Phase 2: Int Joinery / Services 2nd fi	10 days	Fri 19/06/26	Thu 2/07/26
0%	FO: Phase 2: FFE (WC)	3 days	Fri 26/06/26	Tue 30/06/26
0%	**External Works**	**102 days**	**Mon 9/02/26**	**Mon 6/07/26**
0%	EW: Kerbs / hardfill / FRP	20 days	Tue 9/06/26	Mon 6/07/26
0%	EW: Landscaping	10 days	Wed 17/06/26	Tue 30/06/26
0%	**EW: Rear Carparks B58 - B87**	**64 days**	**Mon 9/02/26**	**Thu 30/04/26**
0%	EW: Ground Scan	1 day	Mon 9/02/26	Mon 9/02/26
0%	EW: Isolate existing shed connections	1 day	Tue 10/02/26	Tue 10/02/26
0%	EW: Relocate buried services (provisiona	10 days	Wed 11/02/26	Tue 24/02/26
0%	EW: Demolition of Existing Shed & Concrete Slab (Provisional)	10 days	Wed 25/02/26	Tue 10/03/26
0%	EW: Demolition of existing Kerb	2 days	Wed 11/03/26	Thu 12/03/26
0%	EW: Excavation & Disposal	5 days	Fri 13/03/26	Thu 19/03/26
0%	EW: Installation of Stormwater pipes &	15 days	Fri 20/03/26	Mon 13/04/26
0%	EW: Backfilling & Compaction	3 days	Tue 14/04/26	Thu 16/04/26
0%	EW: Roadbase preparation & Compactio	3 days	Fri 17/04/26	Tue 21/04/26
0%	EW: Kerb installation	3 days	Wed 22/04/26	Fri 24/04/26
0%	EW: Asphalt Works	1 day	Tue 28/04/26	Tue 28/04/26
0%	EW: Line marking	2 days	Wed 29/04/26	Thu 30/04/26
0%	**EW: Rear Carparks B88 - B96**	**42 days**	**Fri 13/03/26**	**Thu 14/05/26**
0%	EW: Demolition of existing Kerb	3 days	Fri 13/03/26	Tue 17/03/26
0%	EW: Excavation & Disposal	2 days	Fri 20/03/26	Mon 23/03/26
0%	EW: Installation of Stormwater pipes &	10 days	Tue 14/04/26	Tue 28/04/26
0%	EW: Backfilling & Compaction	2 days	Wed 29/04/26	Thu 30/04/26
0%	EW: Roadbase preparation & Compactio	3 days	Fri 1/05/26	Thu 7/05/26
0%	EW: Kerb installation	3 days	Fri 8/05/26	Tue 12/05/26
0%	EW: Asphalt Works	1 day	Wed 13/05/26	Wed 13/05/26
0%	EW: Line marking	1 day	Thu 14/05/26	Thu 14/05/26
0%	**Construction Conclusion**	**47 days**	**Tue 12/05/26**	**Fri 17/07/26**
0%	Conclusion: Client / Lessor fit out access - A	1 day	Tue 12/05/26	Tue 12/05/26
0%	Conclusion: Client / Lessor fit out access - I	1 day	Thu 28/05/26	Thu 28/05/26
0%	Conclusion: Test & commission	10 days	Wed 1/07/26	Wed 15/07/26
0%	Conclusion: Final defecting	5 days	Wed 8/07/26	Wed 15/07/26
0%	Conclusion: Final inspections	2 days	Thu 16/07/26	Fri 17/07/26
0%	Conclusion: Practical completion (Target)	0 days	Fri 17/07/26	Fri 17/07/26
0%	**CONTRACT CONCLUSION**	**10 days**	**Fri 17/07/26**	**Fri 31/07/26**
0%	CCC - Lodge application	0 days	Fri 17/07/26	Fri 17/07/26
0%	Weather contingency	10 days	Mon 20/07/26	Fri 31/07/26
0%	Practical Completion (Contract)	0 days	Fri 31/07/26	Fri 31/07/26
